

APIs for Invoicing

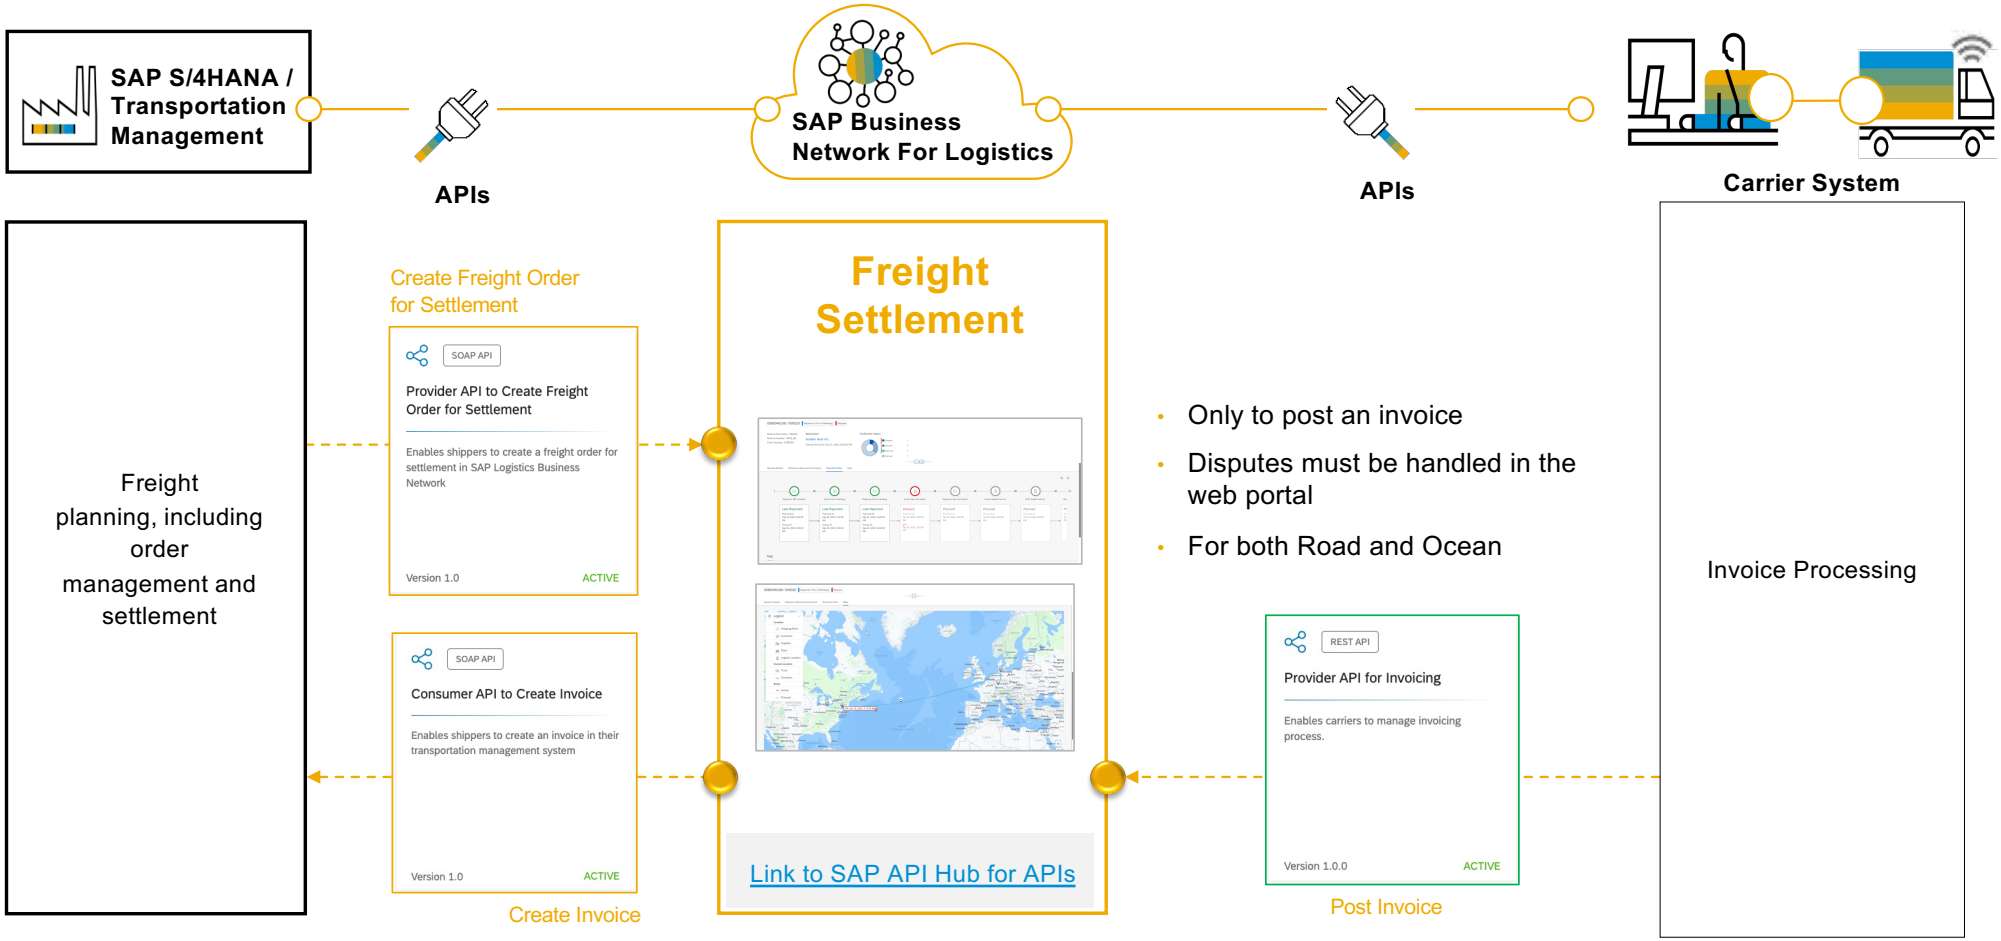

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only


EDI for Invoicing

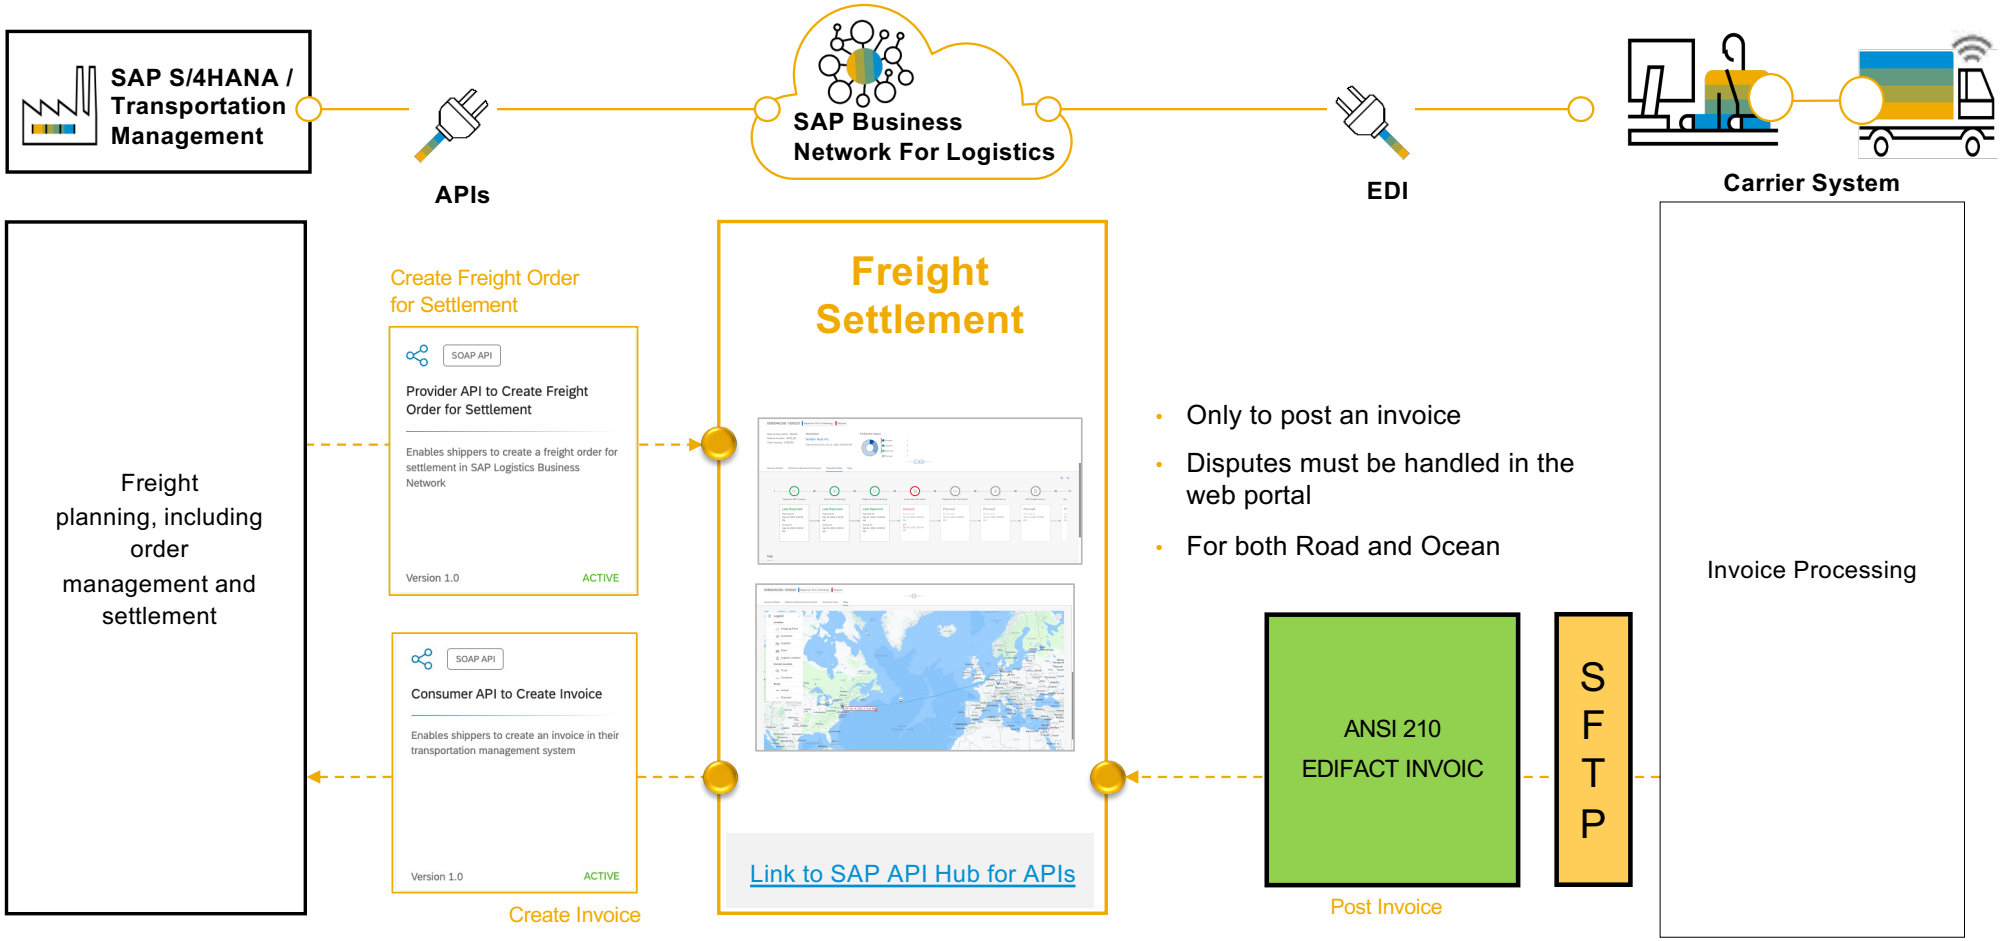


© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

Leverage Freight Forwarders For External Planning

APIs to work directly from your SAP S/4HANA / Transportation Management System

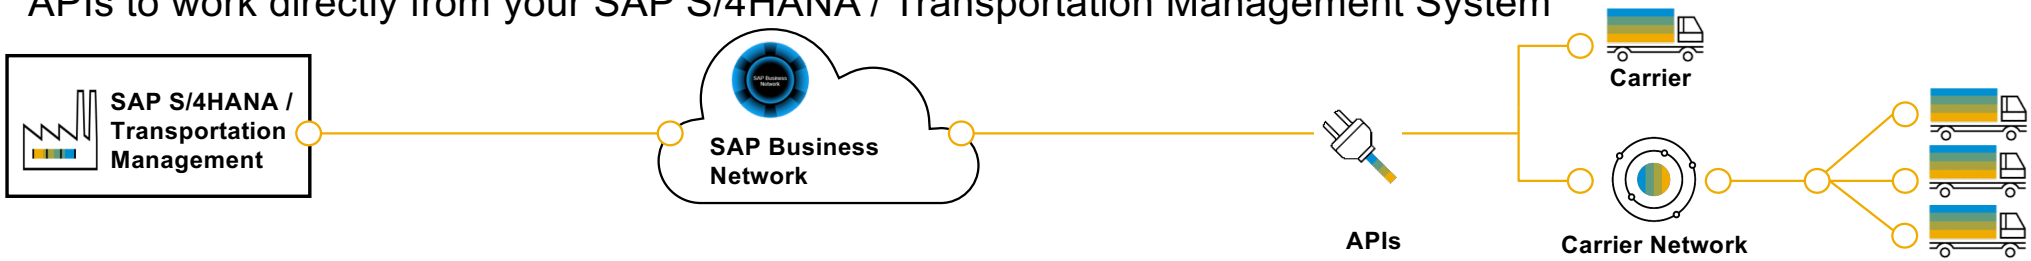

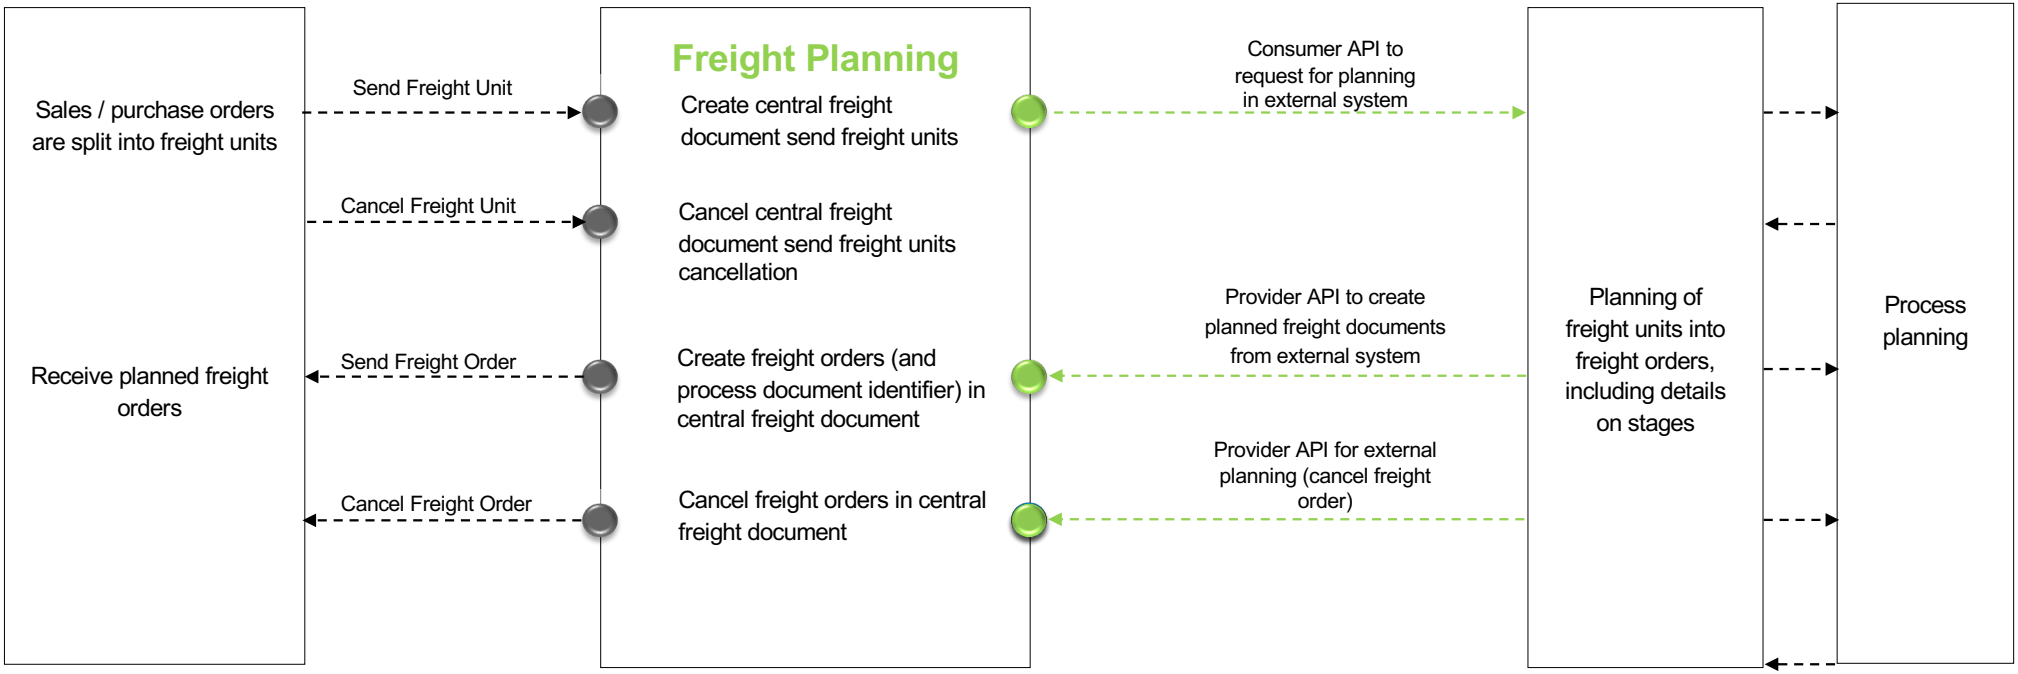


Out-of-the-box integration via 'TransportationOrderGenericRequest'

Link to SAP API Hub for APIs

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Cu[illegible]ers only

Agenda

- Introduction of Logistics Business Network
- Integration Options
- API / EDI Integration Scenarios
- API Flows In Detail
- Roles and Responsibilities
- Project Plan Timeline
- How To Get Started



© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

Shipper and Carrier Roles

Project Lead
Contact for project coordination
Contact for trouble shooting and/or escalations
Commitment to project scope and timeline
Technical Lead
Knowledge of transaction rules and day-today activities
Preform data mapping updates
Trouble shoot system errors ie) document failures
Testing Lead
Ability to access system to create documents for testing
Ability to validate and provide feedback on test documents
Assist in other testing activities
Provide confirmation testing is complete and project can go live
Business Lead
Firsthand knowledge of day-to-day activities
Knowledge of master data procedures
Review and confirm test plan
Attend regular calls as needed
Part of hyper care calls

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

Responsibilities

Phase	Task	SAP	Shipper	Carrier
Discover	Carrier kick-off scheduled	A	R	I
	Provide generic integration samples	R		I
Prepare	Confirm business requirements and documents in scope	R	A	C
	Confirm dates, milestone, target go live	A	R	C
	Confirm project team and resources	A	R	R
	Define test plan and test scenarios	A	R	C
Explore	Confirm carrier test sytem configured *(for all endpoints)*	A		R
	Confirm test scripts include all document scenarios	A	R	R
	Sample fright order to validate connectivity *(SIT testing)*	A	R	R
	Sample invoice to validate connectivity *(SIT testing)*	A	R	R
Realize	Identify & develop mapping enhancements (if any)	R	A	C
	Send test documents per test scripts	A	R	I
	Carrier confirms receipt & validation of documents	A	I	R
	Carrier submits return documents	A	I	R
	Shipper validates returned documents	A	R	I
	*** Repeat relative to test script ***			
	Complete all test script scenarios	A	R	R
	Formal sign off to confirm testing is completed	A	R	R

R - actually carries out the task | A - ultimately accountable | C - Consulted | I - Informed

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

Responsibilities


Phase	Task	SAP	Shipper	Carrier
Deploy	Carrier migrates maps to production	A	I	R
	Confirm carrier account configured in production	A	R	R
	Confirm production LBN ID applied to vendor record in FC/GTT or TM	I	A	C
	Formal sign off for go-live	A	R	R
	Post go-live support process introduced	A	R	I
Change Management Support	Confirm go-live date and share support links	A	R	R
	Confirm support / escalation process	A		R
	Carrier transition to SAP Support	A		R

R - actually carries out the task	A - ultimately accountable	C - Consulted	I - Informed

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only


Agenda

- Introduction of Logistics Business Network
- Integration Options
- API / EDI Integration Scenarios
- API Flows In Detail
- Roles and Responsibilities
- Project Plan Timeline
- How To Get Started




© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

API Integration Implementation Effort Estimate – guidance only



Tendering




10d

Subcontracting




10d

Subcontracting - Booking

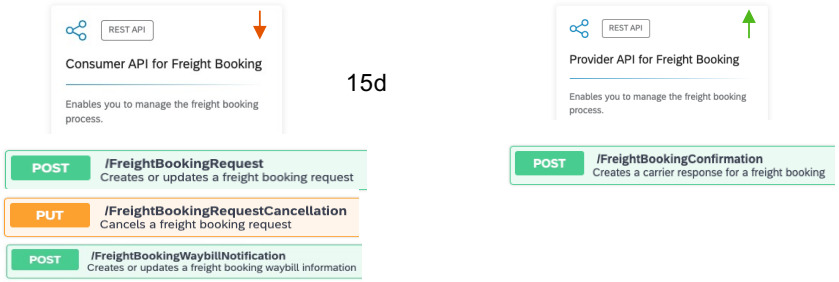


15d

Invoicing



Tracking




↓ **Inbound**

↑ **Outbound**

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only

Note: the efforts can differ based on scenarios, capacity and skillset.

Project Plan Timeline

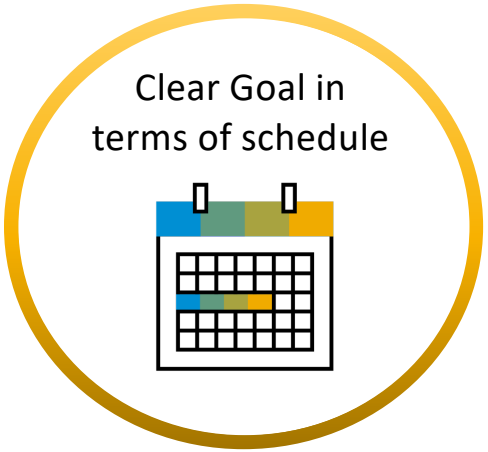

Project Phases	Plan Dates
Average Duration	13-15 weeks
Prepare	Month – Day – Year
Explore	Month – Day – Year
Realize	Month – Day – Year
Deploy	Month – Day – Year

The duration of the project depends on the supplier priority. (i.e. other projects engagement, ERP upgrade, releases, code freeze, vacation, holiday planning, third party involvement)

© 2022 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL - SAP and Customers only
